Data Date: 28-Jun-21

Capitol Paving of D.C., Inc.

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Activity % Complete
Oregon-LA-06-28-1	**Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD 06-28-21)**	200	28-Jun-21	21-Dec-21	04-Nov-20		
Oregon-LA-06-28-1.1	**PRE-CONSTRUCTION PHASE**	0					
Oregon-LA-06-28-1.2	**PROJECT MILESTONES**	9	28-Jun-21	10-Jul-21			
MIL-1030	Finish Phase 2	0		09-Jul-21			0%
MIL-1050	Finish Modified Phase 3B & 3B-1	0		09-Jul-21			0%
MIL-1060	Start Modified Phase 3C & 3C-1	0	10-Jul-21				0%
MIL-1130	Finish Modified Phase 3C-2	0		28-Jun-21			0%
MIL-1140	Start Phase 3A	0	10-Jul-21				0%
Oregon-LA-06-28-1.3	**CONSTRUCTION PHASE**	200	28-Jun-21	21-Dec-21	04-Nov-20		
Oregon-LA-06-28-1.3.7	**Change Orders, Article 3 Directives and Additional Work**	0					
Oregon-LA-06-28-1.3.7.1	**Emergency Resurfacing b/w Military Rd & Horse Stable Rd**	0					
Oregon-LA-06-28-1.3.1	**PHASE 1 (Oregon Ave b/w Beech St & Western Ave NW)**	0					
Oregon-LA-06-28-1.3.1.1	**Phase 1A (Eastern Half b/w Beech St & Western Ave NW)**	0					
Oregon-LA-06-28-1.3.1.2	**Phase 1A-1 (SE Corner- Oregon Ave, Chesnut St & Wise Rd)**	0					
Oregon-LA-06-28-1.3.1.3	**Phase 1A-2 (NE Corner- Oregon Ave, Chesnut St & Wise Rd)**	0					
Oregon-LA-06-28-1.3.1.4	**Phase 1B (Western Half b/w Beech St & Western Ave NW)**	0					
Oregon-LA-06-28-1.3.1.5	**Phase 1B-1 (SW Corner- Oregon Ave, Chesnut St & Wise Rd)**	0					
Oregon-LA-06-28-1.3.1.6	**Phase 1B-2 (NW Corner- Oregon Ave, Chesnut St & Wise Rd)**	0					
Oregon-LA-06-28-1.3.1.7	**Phase 1C (Northen Half of Western Ave)**	0					
Oregon-LA-06-28-1.3.2	**PHASE 2 (Oregon Ave b/w Military Rd & Rittenhouse St NW)**	10	28-Jun-21	09-Jul-21			
Oregon-LA-06-28-1.3.2.1	**Phase 2A (Eastern Half b/w Military Rd & Rittenhouse St NW)**	0					
Oregon-LA-06-28-1.3.2.2	**Phase 2A-1 (Eastern Half- Oregon Ave & Horse Stable Rd)**	0					
Oregon-LA-06-28-1.3.2.3	**Phase 2B (Western Half b/w Military Rd & Rittenhouse St NW)**	0					
Oregon-LA-06-28-1.3.2.4	**Phase 2B-1 (Island Modification - Oregon Ave & Clover Rd)**	9	28-Jun-21	09-Jul-21			
P2B1-1000	Demolish East Side Curb of Existing Island (Military Rd, Oregon Ave & Clover Rd)	7	28-Jun-21	07-Jul-21			0%
P2B1-1010	Install PCC Curb, Gutter; Restore Roadway, Install Directional Island	2	08-Jul-21	09-Jul-21			0%
Oregon-LA-06-28-1.3.3	**PHASE 3 (Oregon Ave b/w Rittenhouse St & Beech St NW)**	152	10-Jul-21	21-Dec-21	10-May-21		
Oregon-LA-06-28-1.3.3.2	**Modified Phase 3B (Eastern Half b/w Rittenhouse St & Tennyson St NW)**	0					
Oregon-LA-06-28-1.3.3.3	**Modfied Phase 3B-1 (Eastern Half - Oregon Ave & Bingham Dr Intersection)**	0					
Oregon-LA-06-28-1.3.3.4	**Modified Phase 3C (Western Half b/w Rittenhouse St & Tennyson St NW)**	30	10-Jul-21	20-Jul-21	07-Jun-21		
MP3C-1020	Install Catch Basins, Basin-Connect & Sewer Pipes, and Manholes (Rittenhouse St to Tennyson St)	12	10-Jul-21	20-Jul-21	21-Jun-21		25%
MP3C-1030	Install Watermain, Fire Hydrants, Gate Valves, Fittings & Appurtenances (Sta. 39+48 to 27+15)	10	10-Jul-21	10-Jul-21	07-Jun-21		95%
MP3C-1040	Install Watermain, Fire Hydrants, Gate Valves, Fittings & Appurtenances (Sta. 27+15 to 17+25)	10	10-Jul-21	10-Jul-21	07-Jun-21		95%
MP3C-1050	Water Service Connections and Replacements (Phase 3C)	2	12-Jul-21	13-Jul-21			0%
MP3C-1060	Roadway Excavation, Install Geotextile, Aggregate Base (3C)	12	12-Jul-21	15-Jul-21	16-Jun-21		70%
MP3C-1070	Install PCC Curb, Gutter, and Wheelchair Ramps	8	12-Jul-21	19-Jul-21	18-Jun-21		20%
MP3C-1075	Install Bioretention Planters, Permeable Pavers, Infiltration Under SW, Underdrains (Tennyson St to Lindsey Dr)	10	12-Jul-21	20-Jul-21	11-Jun-21		25%
MP3C-1080	Install Bioretention Planters, Permeable Pavers, Infiltration Under SW, Underdrains (Lindsey Dr to Rittenhouse St)	10	12-Jul-21	20-Jul-21	11-Jun-21		25%
MP3C-1090	Install Porous Flexible, Exposed Aggregate Sidewalks, & Property Driveway Entrances	5	12-Jul-21	16-Jul-21			0%
Oregon-LA-06-28-1.3.3.5	**Modified Phase 3C-1 (Western Half - Oregon Ave & Bingham Rd Intersection)**	24	10-Jul-21	12-Jul-21	07-Jun-21		
MP3C1-100	Install Watermain, Gate Valves, Fittings & Appurtenances	1	10-Jul-21	10-Jul-21	07-Jun-21		95%
MP3C1-101	Roadway Excavation, Install Geotextile, Aggregate Base (3C-1)	1	10-Jul-21	10-Jul-21	16-Jun-21		70%
MP3C1-102	Install PCC Curb, Gutter, Wheel Chair Ramps, Exposed Sidewalk	1	10-Jul-21	10-Jul-21	18-Jun-21		20%
MP3C1-103	Install 8" HMA Base Course, 19mmn (3C-1)	1	10-Jul-21	12-Jul-21			0%
Oregon-LA-06-28-1.3.3.6	**Modified Phase 3B-2 (Eastern Half of Oregon Ave b/w Tennyson St & Oregon Knolls Dr NW)**	0					
Oregon-LA-06-28-1.3.3.7	**Modified Phase 3C-2 (Western Half of Oregon Ave b/w Tennyson St & Oregon Knolls Dr NW)**	0					

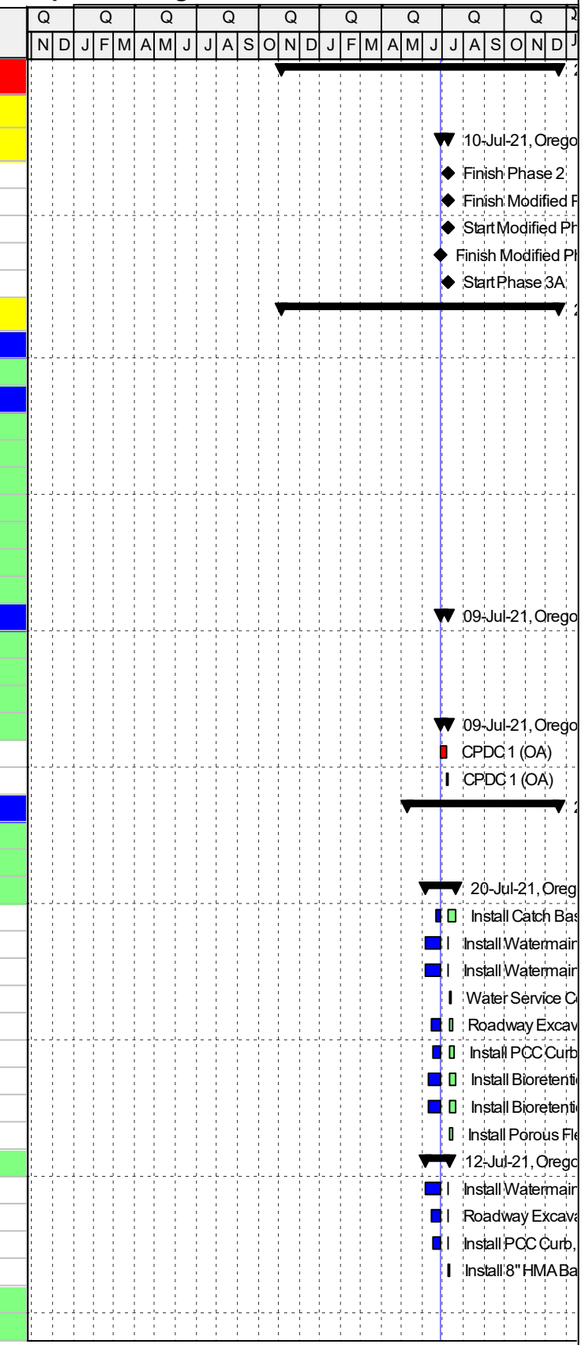

Remaining Level ...
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD 06-28-21)

Oregon-LA-06-28-1

3-Week Look-Ahead© Oracle Corporation

CAPITOL PAVING OF D.C., INC. WASHINGTON, D.C. 20018 202 - 529-7225

Data Date: 28-Jun-21

Capitol Paving of D.C., Inc.

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Activity % Complete
Oregon-LA-06-28-1.3.3.1	**Phase 3A (Bridge Reconstruction of Pinehurst Branch)**	131	10-Jul-21	23-Nov-21	10-May-21		
Oregon-LA-06-28-1.3.3.1.1	**Bridge Work**	7	12-Jul-21	19-Jul-21			
P3A-B-1(	North & South Abutment Install Stream Diversion	3	12-Jul-21	14-Jul-21			0%
P3A-B-1(	North & South Abutment Excavation	4	15-Jul-21	19-Jul-21			0%
Oregon-LA-06-28-1.3.3.1.2	**Utility Work & Civil Work**	131	10-Jul-21	23-Nov-21	10-May-21		
P3A-SW-	Install Sewer Manhole, 21" Sanitary Sewer, and Outfalls 5 & 6 (3A)	10	10-Jul-21	10-Jul-21	10-May-21		90%
P3A-SW-	Install Electric Manholes, Conduits, and Concrete Enclosures (3A)	12	13-Nov-21	23-Nov-21	09-Jun-21		25%
Oregon-LA-06-28-1.3.3.8	**Phase 3E (Entire Roadway Section b/w Oregon Knolls Dr & Private Driveway)**	23	07-Dec-21	21-Dec-21	27-May-21		
P3E-1015	Install Electric Conduits, and Concrete Enclosures	10	07-Dec-21	08-Dec-21	27-May-21		85%
P3E-1070	Install Retaining Wall No. 3, Stone Faced Coping, Stockade Wood Fence	10	11-Dec-21	21-Dec-21	15-Jun-21		10%
Oregon-LA-06-28-1.3.4	**Traffic & Streetlight Work**	14	10-Jul-21	24-Jul-21	04-Nov-20		
TR-1050	Install Traffic Foundation, Cabinet, Controller, Pole, Lights (Oregon Ave & Military Rd)	14	10-Jul-21	24-Jul-21	04-Nov-20		20%
Oregon-LA-06-28-1.3.5	**Paving, Line Stiping, Signage, and Miscellaneous Work**	0					
Oregon-LA-06-28-1.3.6	**Landscape Work**	0					
Oregon-LA-06-28-1.4	**LUMPSUM ITEMS (Non-Construction)**	0					
Oregon-LA-06-28-1.5	**POST-CONSTRUCTION PHASE**	0					
Oregon-LA-06-28-1.6	**Delays, Additional Work, and Changes**	5	28-Jun-21	03-Jul-21			

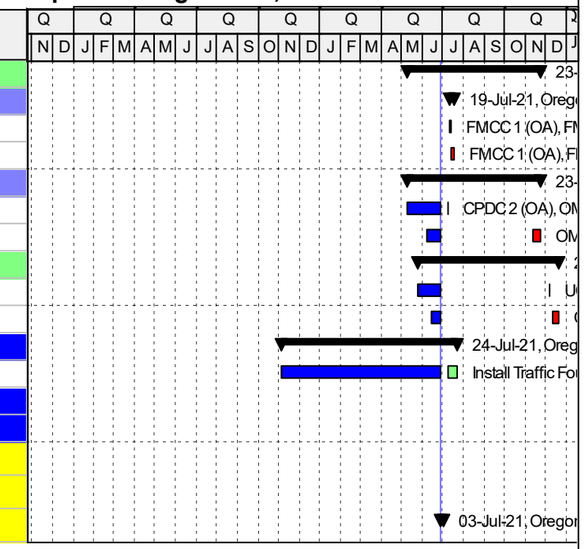

Remaining Level ...
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD 06-28-21)

Oregon-LA-06-28-1

3-Week Look-Ahead© Oracle Corporation
